



AGRICULTURE GLOBAL PRACTICE TECHNICAL ASSISTANCE PAPER

BEYOND QUALITY AT ENTRY

PORTFOLIO REVIEW ON GENDER IMPLEMENTATION OF AGRICULTURE PROJECTS (FY08–13)

Ingrid Mollard, Emily Brearley, Marialena Vyzaki, and Sanna-Liisa Taivalmaa

WORLD BANK GROUP REPORT NUMBER 94753-GLB

APRIL 2015



THE WORLD BANK
IBRD • IDA | WORLD BANK GROUP

AGRICULTURE GLOBAL PRACTICE TECHNICAL ASSISTANCE PAPER

BEYOND QUALITY AT ENTRY

Portfolio Review on Gender Implementation of Agriculture Projects (FY08–13)

Ingrid Mollard, Emily Brearley, Marialena Vyzaki, and Sanna-Liisa Taivalmaa



THE WORLD BANK
IBRD • IDA | WORLD BANK GROUP

© 2015 World Bank Group

1818 H Street NW
Washington, DC 20433
Telephone: 202-473-1000
Internet: www.worldbank.org
Email: feedback@worldbank.org

All rights reserved

This volume is a product of the staff of the World Bank Group. The findings, interpretations, and conclusions expressed in this volume do not necessarily reflect the views of the Executive Directors of World Bank Group or the governments they represent.

The World Bank Group does not guarantee the accuracy of the data included in this work. The boundaries, colors, denominations, and other information shown on any map in this work do not imply any judgment on the part of World Bank Group concerning the legal status of any territory or the endorsement or acceptance of such boundaries.

Rights and Permissions

The material in this publication is copyrighted. Copying and/or transmitting portions or all of this work without permission may be a violation of applicable law. World Bank Group encourages dissemination of its work and will normally grant permission to reproduce portions of the work promptly.

For permission to photocopy or reprint any part of this work, please send a request with complete information to the Copyright Clearance Center, Inc., 222 Rosewood Drive, Danvers, MA 01923, USA, telephone: 978-750-8400, fax: 978-750-4470, <http://www.copyright.com/>.

All other queries on rights and licenses, including subsidiary rights, should be addressed to the Office of the Publisher, World Bank Group, 1818 H Street NW, Washington, DC 20433, USA, fax: 202-522-2422, e-mail: pubrights@worldbank.org.

Cover images from left to right: Charlotte Kesi/World Bank, Colombia; Curt Carnemark/World Bank, India; Wu Zhiyi/World Bank, China.

CONTENTS

Acknowledgments	v
Abbreviations and Acronyms	vii
Executive Summary	ix
Chapter One: Introduction	1
Gender Mainstreaming in Agriculture and Rural Development: Why Is It Important?	1
Tracking Gender at the Design Stage (Quality at Entry)	1
Gender at Entry in International Development Association and Agriculture Sector Projects	3
Objective of the Gender in Implementation Review	4
Chapter Two: A New Tool to Track Gender in Implementation	7
Why Develop a New Tool for Tracking Gender in Project Implementation?	7
How to Use the QAI Tool to Track Gender in Implementation	7
Chapter Three: Findings of the Gender in Implementation Review	11
Results of the Gender in Implementation Review by Region	11
Results by Gender Informed versus Gender Implemented Rating	13
Results by Gender Dimension	14
Gender Tracking of Implementation and Completion Reports	18
Gender Content in the Key Documents Reviewed	18
Chapter Four: Gender Implemented: Baseline and Targets	21
Chapter Five: Conclusions and Discussion	23
Chapter Six: Recommendations	25
References	27
Appendix A: Good Practice Examples	29
Appendix B: Types of Documents Reviewed	31
Appendix C: Sample Selection of Projects	33
BOX	
Box 1.1: IDA17 Gender Commitments	3
FIGURES	
Figure 3.1: Projects Rated Gender Implemented, by Region	13
Figure 3.2: Gender Informed and Gender Implemented Projects, by Region	13
Figure 3.3: Percentage of Projects by Gender Informed/Gender Implemented Category	13
Figure 3.4: Percentage of Projects by Gender Informed/Gender Implemented Category and Region	13
Figure 3.5: Projects Conducting Gender Analysis at Implementation	14
Figure 3.6: Relationship between Gender Analysis and Gender Actions during Project Implementation, by Region	14

Figure 3.7: Characteristics of Projects with No Gender Activities, by Region	14
Figure 3.8: Projects That Scored 1 on the Gender Actions Dimension, by Region	15
Figure 3.9: Gender Actions, by Region	15
Figure 3.10: Distribution of Projects That Did/Did Not Mention Actions to Mainstream Gender in Project Documents	16
Figure 3.11: Projects That Scored 1 on the Gender M&E Dimension, by Region	16
Figure 3.12: Gender M&E Activities, by Region	17

TABLES

Table 1.1: Quality at Entry: Checklist for Gender Rating of Operations	2
Table 1.2: Gender Integration in New Agriculture Projects (FY10/12): Share of Satisfactory Projects in Each Dimension Compared to Agriculture Action Plan's (2013–15) Targets	4
Table 2.1: Gender in Implementation: Documents Reviewed	9
Table 2.2: Gender in Implementation and Completion: Checklist for Rating Projects	9
Table 3.1: Gender Mainstreaming in Implementation: Examples of Gender Actions	12
Table 4.1: Suggested Gender Implemented Targets	21
Table A.1: Zambia, Irrigation Development and Support Project Aide-Mémoire: Agreed Gender Actions (2011)	30
Table C.1: Africa Region Project Sample for Review	34
Table C.2: East Asia and Pacific Region Project Sample for Review	34
Table C.3: Europe and Central Asia Region Project Sample for Review	35
Table C.4: Latin America and Caribbean Region Project Sample for Review	35
Table C.5: Middle East and North Africa Region Project Sample for Review	35
Table C.6: South Asia Region Project Sample for Review	36
Table C.7: Project Sample Selection for Reviewing Implementation Completion Reports	36

ACKNOWLEDGMENTS



This paper was developed and managed by Eija Pehu (Task Team Leader [TTL], GFADR) and Pirkko Poutiainen (co-TTL) from the Agriculture Global Practice (formerly Agriculture and Environmental Services Department), who provided continuous guidance throughout the project. It was written by a team of World Bank staff and consultants comprised of Ingrid Mollard (Consultant, GFADR), Emily Brearley (Consultant, GSURR), Marialena Vyzaki (Consultant, GFADR), and Sanna-Liisa Taivalmaa (Senior Gender Specialist, GFADR).

The team would like to extend its gratitude to the peer reviewers, acting in their personal capacity, for their helpful and insightful feedback on gender mainstreaming in World Bank operations: Achim Fock (Manager, SARDE), Svetlana Edmeades (Senior Agriculture Economist, GFADR), Elena Bardasi (Senior Economist, IEGPS), Melissa Williams (Senior Rural Development Specialist, GFADR), Anis Wan (Operations Officer, GENDR). The report was edited by Kelly Cassaday, and the publication process was managed by Jim Cantrell (Communications Analyst, ENRGP).

ABBREVIATIONS AND ACRONYMS

AES	Agriculture and Environmental Services
AFR	Africa
AM	Aide-Mémoire
ARD	Agriculture and Rural Development
CCSA	Cross-Cutting Solution Area
EAP	East Asia and the Pacific
ECA	Europe and Central Asia
FY	Fiscal Year
GENRD	Gender in Rural Development
GIL	Gender Innovation Lab
ICR	Implementation and Completion Report
IDA	International Development Association
IDSP	Irrigation Development and Support Project
IEG	Independent Evaluation Group
ISR	Implementation Status and Results Report
LCR	Latin America and Caribbean
MACO	Ministry of Agriculture and Cooperatives

M&E	Monitoring and Evaluation
MNA	Middle East and North Africa
MTR	Midterm Review
NGO	Non-Governmental Organization
NIA	National Irrigation Administration
PAD	Project Appraisal Document
PDO	Project Development Objective
PIDP	Participatory Irrigation Development Project
PIM	Project Implementation/Operations Manual
PREM	Poverty Reduction and Economic Management
QAE	Quality at Entry
QAI	Quality at Implementation
SAR	South Asia
TOR	Terms of Reference
TTL	Task Team Leader
WUA	Water User Association

All dollar amounts are U.S. dollars unless otherwise indicated.

EXECUTIVE SUMMARY



The objective of this study was to go beyond a standard gender review of project design to increase knowledge of how and to what extent World Bank agriculture projects address gender issues during implementation. The study **introduces a tool to track gender mainstreaming in the implementation phase** of a project. The tool is then used to **review the portfolio of current agriculture projects, establish a baseline,** and **suggest targets for gender mainstreaming** for the future portfolio.

A TOOL FOR TRACKING GENDER IN IMPLEMENTATION: QUALITY AT IMPLEMENTATION

The Quality at Implementation (QAI) tool builds on the World Bank’s corporate-level analysis of gender integration at the design stage—the review of Project Appraisal Documents (PAD) that is carried out before a project is approved. In these Quality at Entry (QAE) reviews, a project is rated “**Gender Informed**” if the Project Appraisal Document addresses gender issues.

The Gender in Implementation tracking tool presented here focuses on the World Bank’s main operational documents—Aide-Mémoires (AMs), Implementation Status and Results (ISRs) reports, Project Implementation/Operation Manuals (PIMs), and Implementation and Completion Reports (ICRs)—to determine if concrete gender actions were included in project implementation. As in the QAE analysis, the QAI tracking tool analyzes three dimensions of gender. First, are gender issues identified or analyzed in studies or reports? Second, are any gender actions undertaken? Third, is monitoring and evaluation (M&E) gender sensitive (for example, did the project involve disaggregated data, specific gender indicators, or special evaluation studies)? Unlike QAE, in scoring the three dimensions equally, the “gender actions” dimension is weighted more heavily than the other two in QAI. A project is rated “**Gender Implemented**” if the operational documents report on gender actions and include at least one of the other two gender dimensions.

The study has some limitations. The QAI review provides information on the extent of gender mainstreaming **based on information provided in AMs, ISRs, and PIMs**. These documents do not always reflect the real situation in the field, as the quality and extent of reporting varies considerably across projects. Also, the number of projects selected differed by region due to differences in the size of their agriculture portfolios. Even so, the QAI tool provides a general picture of gender mainstreaming in implementation in the agriculture portfolio. Lastly, the QAI analysis stops at the outcome level and cannot be used to track the actual impacts of the gender actions that were implemented. Such evaluation is done with special impact assessments after a project closes.

RESULTS OF THE PORTFOLIO REVIEW

The World Bank's agriculture portfolio had 236 active projects between fiscal years FY08 and FY13, of which 55 projects, representing 26.45 percent of the net commitment (\$5.53 billion), were selected for review. In addition, 14 ICRs were analyzed.

Seventy-six percent of the projects were scored Gender Implemented. The quality of the implementation varied greatly, however. A project that was Gender Informed at entry did not guarantee that gender actions were implemented (11 percent of projects reviewed), although such projects were more likely to integrate gender actions in implementation.

Gender actions were included in 69 percent of the projects reviewed. However, 11 percent of the projects reviewed were neither Gender Informed at the design stage nor Gender Implemented, despite the World Bank's policy commitment to mainstream gender.

Gender in M&E systems was weak and inconsistent. Only 42 percent of the projects monitored the World Bank's core compulsory "Direct project beneficiaries (number), of which female (percentage)" gender indicator. Moreover, results frameworks were largely inadequate in terms of the number of gender-disaggregated indicators and the number and quality of indicators specifically designed to track outcomes for women. In some cases, quantitative

and qualitative data on outcomes for women were collected through special studies, focus group discussions, and specific analyses to improve gender mainstreaming and/or scale-up of successful approaches.

The portfolio analysis and communication with task team leaders (TTLs) found that the main factors for satisfactory rating for gender implementation were:

- » Including a gender specialist or a sector expert with gender skills as part of the implementation support team;
- » Conducting a gender analysis during the implementation phase;
- » Reporting systematically on gender in AMs and ISRs;
- » Including gender actions and processes in PIMs; and
- » Allocating resources explicitly for gender-specific activities to support implementation.

As mentioned, the review included a small, randomly selected sample (14) of ICRs. In contrast to the implementation documents, most of the ICRs contained a significant amount of information on gender mainstreaming, reported in a designated section on gender issues under the project. This finding highlights an important point. Because the implementation reporting documents (AMs and ISRs) do not have a dedicated section for gender and because task teams are not encouraged to report on gender in project documents, they do not always capture information on gender. Consequently, some of the World Bank's achievements in gender are underreported, and potential lessons are lost.

GENDER IMPLEMENTATION TARGETS

As with the QAE, senior management of the Agriculture Global Practice could consider setting gender QAI targets. Targets could be set to 95 percent of projects by FY18 for gender analysis, actions, and M&E during implementation. Given the analysis conducted during implementation is need-based, it could also form part of the M&E evaluations/studies. It is therefore suggested that the QAI analysis rating builds on the QAE analysis rating.

RECOMMENDATIONS

1. Overall, it is important to expand gender tracking throughout the project cycle.

Continued and deepened regular analyses of agriculture projects during the concept note stage, during the quality at entry steps (Quality Enhancement Reviews, Project Appraisal Documents), and during implementation—up to the ICR, where best practices can be identified—is proven to strengthen strategic gender implementation and outcomes. Harmonizing portfolio review methodologies at entry, implementation, and project closing improves our understanding of the consistency of gender mainstreaming in agriculture projects.

2. Use the Gender in Implementation tracking tool to identify gender gaps in order to provide proactive support to TTLs.

The tool can identify projects performing poorly on gender issues during implementation and can garner support for TTLs. It is suggested that a review of gender implementation in the agriculture portfolio be conducted every second year. The Gender Cross-Cutting Solution Area; the Urban, Rural, and Social Development Global Practice; and the Agriculture Global Practice are encouraged to regularly review Gender Informed (at design) and Gender Implemented scores and to agree on how to proactively provide support to poorly performing projects. The methodology presented here can also be applied at the midterm of a project to quickly gain an understanding of the situation in a given project and change course, if needed, before the project closes.

3. Ensure gender skills, tools, and funding for each project.

For project staff, training in gender skills and concrete actions as well as in strategies for overcoming possible obstacles to gender implementation is essential. It is important to develop user-friendly tools for TTLs; for example, checklists to review progress on gender in implementation at the midterm review (MTR) stage, to monitor gender during implementation, and to provide sample terms of reference for the

recruitment of gender specialists. Furthermore, it is suggested that a pool of gender expertise could be established to provide resources for such support. However, the ultimate goal is for project and supervision budgets to allocate resources explicitly to support gender actions.

4. Management has a responsibility to take action on gaps in gender mainstreaming.

It is important to sensitize management and provide tools and guidance on how to review project documents (that is, Project Appraisal Documents, Aide-Mémoires, Implementation Status Reports, Implementation and Completion Reports) with a gender lens and suggest remedial action as needed. Such interaction between management and TTLs is also an opportunity to build commitment to monitor gender progress, and it has the potential to increase staff accountability to enhance gender mainstreaming. In addition, the Independent Evaluation Group (IEG) is well positioned to increase gender mainstreaming in implementation within the World Bank by consistently reviewing projects in terms of quality of gender in implementation and completion. It is suggested that IEG continues to emphasize gender as a thematic issue by systematically tracking how gender is addressed in projects and which results are achieved. Increasing the weight of gender mainstreaming in project ratings has the potential to incentivize TTLs to integrate gender in implementation. At the same time, task teams need to fully use the ICR to report on gender, using the dedicated field “Poverty, social, and gender impacts” in addition to the matrix of indicators.

5. Improve gender reporting within the World Bank system.

Encourage TTLs to report on gender in Aide-Mémoires. Systematized reporting will give a better understanding of the real situation of gender mainstreaming and thus support reducing under- and overreporting. A potential revision of the Aide-Mémoire Guidelines for reporting progress on gender issues, actions, and recommendations to government could be accompanied with a short training session for users (for example, in the form of e-learning).

6. Secure a robust M&E system that deploys diverse tools, including quantitative and qualitative methods to assess gender issues, progress, and achievements. The M&E system of a project needs to develop gender-sensitive indicators along the entire results chain, to use a diverse set of tools, and to collect a variety of data to assess gender outcomes. At the same time, it is very important to learn from the impact evaluation studies being conducted by the Gender Innovation Lab (GIL) and others to increase the knowledge of what does and does not work. It is necessary to identify any gender-related impediments for project benefits throughout implementation, to investigate the issues, and to propose solutions so that these gender asymmetries can be removed or mitigated.

7. Systematize links between the World Bank's gender experts. To generate positive synergies, it

is essential to create working relationships among the World Bank's gender experts from the Agriculture Global Practice; the Gender Cross-Cutting Solution Area; the Urban, Rural, and Social Development Global Practice; and the other global practices and Cross-Cutting Solution Areas (CCSAs). Greater synergy would allow gender expertise to be engaged more broadly and for lessons and good practices to be shared and disseminated more widely, within and across the regions and sectors.

8. The Agriculture Global Practice should set targets for gender implementation. Setting targets derived from the baseline established in this review can incentivize projects and regions to improve their performance and monitor progress against agreed targets. Unit and staff accountability for gender mainstreaming can be enhanced by such targets and can be one way to reach the desired development outcomes.

CHAPTER ONE

INTRODUCTION

GENDER MAINSTREAMING IN AGRICULTURE AND RURAL DEVELOPMENT: WHY IS IT IMPORTANT?

The *World Development Report 2012: Gender Equality and Development* (World Bank 2011) argues that **greater gender equality is not just the right thing to do but is also good for the economy**. Greater gender equality can enhance productivity, improve development outcomes for the next generation, and make institutions more representative. Women account for 43 percent of the world's agricultural labor force (FAO 2011). Increased gender equality in agriculture can significantly contribute to increased production and profits, the adoption of new technologies, and higher household incomes. These outcomes are important because resources and incomes controlled by women are more likely to be used to improve family food consumption and welfare, reduce child malnutrition, and increase overall family well-being.

The agriculture sector is underperforming in many developing countries, in part because men and women do not have equal access to the resources and opportunities they need to be productive. Across countries and contexts, women have consistently less access than men to agricultural assets, inputs, and services and to rural employment opportunities. Increasing women's access to land, water, livestock, inputs, education, financial services, agricultural extension information, technology, labor, and rural employment would boost their productivity and generate gains in agricultural output, food security, economic growth, and social welfare (O'Sullivan et al 2014). If women had the same access to productive resources as men, they could increase yields on their farms by 20–30 percent (FAO 2011).

TRACKING GENDER AT THE DESIGN STAGE (QUALITY AT ENTRY)

At the corporate level, the World Bank tracks gender at the Quality at Entry stage (QAE) of the project cycle. Before projects are approved, all Project Appraisal Documents are analyzed using the QAE methodology, which focuses

TABLE 1.1. QUALITY AT ENTRY: CHECKLIST FOR GENDER RATING OF OPERATIONS

Gender Dimension	Criteria for Rating Project: <i>The Activity . . .</i>	Guiding Questions: <i>Does the Project . . .</i>	Check	Score 1/0
Gender analysis	Includes analysis and/or consultation on gender-related issues.	- Identify and analyze gender issues <i>relevant</i> to the project objectives or components? - Report findings of country/regional gender diagnostics (gender assessment, poverty assessment, and so forth) relevant to project development objectives or components, or does the project undertake a social or environmental or poverty and social impact assessment? - Reflect the results of consultations with women/girls/men/boys and/or Non-Governmental Organizations (NGOs) that focus on these groups and/or specific line ministries?		1/0
• If at least one check above, a score of 1 is achieved				
Gender actions	Is expected to narrow gender disparities, including through specific actions to address the distinct needs of women/girls/men/boys and/or to have positive impact(s) on gender equality.	- Include specific or targeted actions that address the needs of women/girls or men/boys? - Propose gender-specific safeguards in a social/environmental assessment or in a resettlement framework? - Show how interventions are expected to narrow existing gender disparities?		1/0
• If at least one check above, a score of 1 is achieved				
Gender monitoring and evaluation	Includes mechanisms to monitor gender impact and facilitate gender-disaggregated analysis.	- Include specific gender and sex-disaggregated indicators in the results framework? - Propose an evaluation, which will analyze the gender-specific impacts of the project?		1/0
• If at least one check above, a score of 1 is achieved				
Overall score	In how many dimensions does the project score 1?			0–3
• The project must score 1 in at least one dimension to be rated Gender Informed by Gender Cross-Cutting Solution Area			Y/N	
• The project must score 3 to be rated Gender Informed by Agriculture Global Practice				

Source: Poverty Reduction and Economic Management (PREM) Network's Gender Group, World Bank.

on three dimensions of gender: gender analysis, gender actions, and gender monitoring and evaluation. With respect to each of these dimensions, projects are rated according to a binary scale that takes a value of 1 if the assessment is positive and 0 if it is not. Overall, projects are considered to be Gender Informed if they score 1 in at least one of the three dimensions (table 1.1).

Gender is tracked at entry through a quarterly computerized review of new projects by the Gender Cross-Cutting Solution Area,¹ conducted in collaboration with the sectors. The methodology was originally developed by the Gender in Rural Development (GENRD) Thematic

¹ Previously, PREM Gender conducted the review.

Group of the World Bank's Agriculture and Rural Development (ARD) department in 2002.

In addition to the QAE rating by the Gender Cross-Cutting Solution Area, the Agriculture Global Practice Management Team² has reviewed Project Appraisal Documents since 2012, scoring them by the same methodology but rating them more rigorously. The Gender Cross-Cutting Solution Area considers a project Gender Informed when it includes at least one of the gender dimensions, whereas the Agriculture Global Practice requires a project to cover all three dimensions to be scored Gender Informed.

GENDER AT ENTRY IN INTERNATIONAL DEVELOPMENT ASSOCIATION AND AGRICULTURE SECTOR PROJECTS

INTERNATIONAL DEVELOPMENT ASSOCIATION (IDA)

The QAE assessments reveal significant progress in integrating gender into IDA Project Appraisal Documents (PADs), consistent with the IDA16³ commitments. Across IDA projects, 86 percent were Gender Informed in FY12, representing about \$12.9 billion (90 percent) of IDA commitments, compared to 72 percent of projects and \$10.9 billion (75 percent) of IDA commitments in FY10. Almost all regions and networks have seen the share of Gender Informed projects increase over the period. A significant deepening of gender mainstreaming in the lending portfolio is evident as well, with about 55 percent of IDA operations approved in FY12 for being Gender Informed in all three dimensions—almost double the share in the preceding two years.

Gender remains a special theme under IDA17,⁴ and the World Bank management has committed to redoubling efforts to reduce gender gaps and to expand gender equality. Building on the progress in IDA16, management will raise the bar on gender

BOX 1.1. IDA17 GENDER COMMITMENTS

To better monitor actions on gender for IDA countries in particular, management proposes the following:

- All IDA country strategies will draw on and discuss the findings of a gender assessment, and at least two-thirds will have highly satisfactory integration of gender, by integrating gender considerations into the analysis, content of the program, and the results frameworks.
- Deepen integration of gender into lending operations so that at least two-thirds of IDA operations have gender-informed analysis and follow-up.
- All regions implement and monitor Regional Gender Action Plans.
- Strengthen knowledge of what does and does not work in IDA countries through monitoring and evaluation, including impact evaluations on gender-related issues, tracking of gender results of IDA operations using gender-disaggregated core sector indicators, and expanded use of beneficiary feedback mechanisms.
- Roll out statistical activities to increase gender-disaggregated data and gender statistical capacity in at least 15 IDA countries.

The Results Measurement System for IDA countries will include new gender-related indicators:

- **Tier 1:** Gender-disaggregated data for two indicators (employment-to-population ratio and bank accounts per 1,000 adults; see above) and contraceptive prevalence for women aged 15–49 years.
- **Tier 2:** Proportion of IDA country strategies that draw on and discuss the findings of a gender assessment; proportion of IDA country strategies that incorporate gender considerations into the analysis, content of the program, and the results framework; and proportion of IDA operations that have gender-informed analysis and follow-up.

*Source: World Bank (2013). *Special Themes for IDA17*.*

integration in IDA's work at the country, regional, and corporate levels, with a special focus on the economic sectors that have been lagging and yet are particularly important for women's economic empowerment. The new gender commitments for IDA17 (box 1.1) will promote transformational change, expanding the frontiers of gender-related knowledge and evidence and building on what works to improve gender equality. Gender must be more deeply integrated into lending operations so that at least two-thirds of IDA operations have gender-informed analysis and follow-up.

² Previously, ARD Sector Board conducted the review.

³ IDA16 was implemented from July 2011 to June 2014.

⁴ IDA17 is implemented from July 2014 to June 2017.

TABLE 1.2. GENDER INTEGRATION IN NEW AGRICULTURE PROJECTS (FY10/12): SHARE OF SATISFACTORY PROJECTS IN EACH DIMENSION COMPARED TO AGRICULTURE ACTION PLAN'S (2013–15) TARGETS

Region	Analysis (Target 2015 = 100%)		Actions (Target 2015 = 75%)		Monitoring and Evaluation (Target 2015 = 75%)		All Three Dimensions (Target 2015 = 75%)	
	Average FY10/12	Baseline 2013	Average FY10/12	Baseline 2013	Average FY10/12	Baseline 2013	Average FY10/12	Baseline 2013
AFR	73	85	80	100	90	100	56	85
EAP	39	100	50	60	29	60	18	40
ECA	62	67	46	100	54	100	31	67
LAC	81	86	81	86	71	86	48	86
MNA	71	100	86	100	71	100	71	100
SAR	80	100	90	100	63	83	57	83
Grand total	68	87	74	92	65	89	46	76

Source: World Bank (2014).

Note: AFR = Africa Region; EAP = East Asia and the Pacific; ECA = Europe and Central Asia; LAC = Latin America and Caribbean; MNA = Middle East and North Africa; SAR = South Asia Region.

AGRICULTURE SECTOR

For agriculture projects, QAE ratings done at the corporate level are considerably higher than those done by the Agriculture Global Practice.⁵

According to the Gender Cross-Cutting Solution Area,⁶ 95 percent of agriculture projects initiated in FY13 were rated Gender Informed under the QAE rating system reviews, compared to 76 percent of projects under the Agriculture Global Practice rating system. *This finding indicates that covering only one gender dimension does not give the full picture of gender mainstreaming in projects.*

Over the years, agriculture projects have shown significant improvement in QAE in all regions.

Agriculture Global Practice analysis shows that in FY13, among regions, East Asia and the Pacific (EAP), the Middle East and North Africa (MNA), and the South Asia Region (SAR) met the analysis target (100 percent), while Africa (AFR), the Latin America and Caribbean (LAC), MNA, and SAR met the target (75 percent) of treating all three dimensions satisfactorily. All regions showed improvements over the baseline years. The other two dimensions of gender in design saw improvements in performance as

well—92 percent of agriculture projects had satisfactory gender actions, and 76 percent had gender-disaggregated indicators in M&E (the latter up from 46 percent over FY10/12) (table 1.2).

OBJECTIVE OF THE GENDER IN IMPLEMENTATION REVIEW

The objective of this study was to go beyond a standard gender review of project design. The goal was to increase knowledge of how and to what extent World Bank agriculture projects address gender issues during implementation **by tracking how gender activities and outcomes are recorded in the World Bank's official reporting system.** A new tool was created for this purpose, based on the methodology of QAE, and is presented here with results from a sample of agriculture projects during the time of the review.

The Agriculture Global Practice has consistently recognized that mainstreaming gender and its tracking is important for projects to succeed. The Agriculture Action Plan (2013–15) explicitly emphasizes the importance of reducing gender inequality in access to assets, services, collective action, and opportunities. The plan specifies key actions to increase the share of agriculture and rural development projects by 2015. That will

⁵ Previously the Agriculture and Rural Development Sector.

⁶ Previously PREM Gender.

(1) include gender analysis in its design, with a target of 100 percent, and (2) include gender mainstreaming in all three dimensions of design (analysis, actions, and M&E), with a target of 75 percent. The reason for the 75 percent target is that gender analysis conducted at entry, for a relatively small set of projects, can reveal that gender-specific actions and related M&E are not needed. The focus on all three elements of design raises the bar for an agriculture project beyond the World Bank standard of satisfactorily addressing at least one of these elements. In addition, from FY15, all agriculture projects will be reviewed by the Gender team in the Agriculture Global Practice (GFADR) in terms of gender mainstreaming at Concept Note, Preparation, and Appraisal stages.

Currently, the World Bank has limited real data at the corporate level to gauge how gender mainstreaming is actually implemented in projects. At the implementation stage, gender mainstreaming can be measured by monitoring some of the Core Sector Indicators relating to beneficiaries because they are supposed to be disaggregated by gender. Close monitoring of these indicators against targets specified in appraisal and implementation documents could provide information on gender mainstreaming in project implementation. However, it has long been recognized that for gender issues to truly gain traction, they must be fully integrated into the core design and components of a project with indicators and targets that are clear, specific to each component, and gender sensitive.

CHAPTER TWO

A NEW TOOL TO TRACK GENDER IN IMPLEMENTATION

WHY DEVELOP A NEW TOOL FOR TRACKING GENDER IN PROJECT IMPLEMENTATION?

The QAE methodology reflects how well gender is integrated into a project's design, but not beyond. The QAE assessment produces a clear picture of how a project proposes to address gender issues, which is a first and significant step for understanding how gender is addressed at the corporate level. The full integration of gender into the Bank's lending operations is still a work in progress. No established methodology and system exist to track gender mainstreaming after the design phase (that is, during a project's implementation and at closure, which arguably are the most important stages of an intervention). It is not known how and to what extent "Gender Informed" at entry translates into "Gender Implemented" during implementation.

The Quality at Implementation (QAI) tool complements the QAE "Gender Informed" rating with a "Gender Implemented" rating. The QAI tracking tool, which is based on the QAE methodology, tracks gender mainstreaming throughout the project cycle, from implementation to completion, by looking at three gender dimensions: gender analysis, gender actions, and gender M&E.

HOW TO USE THE QAI TOOL TO TRACK GENDER IN IMPLEMENTATION

The QAI tracking tool can be used to complement the QAE methodology for periodically reviewing and tracking gender mainstreaming during implementation of projects in the agriculture portfolio (or the portfolio of any Global Practice). The tool could also be used at the project midterm review to track gender implementation and identify any support or actions needed to attain successful gender outcomes.

It is worth noting that the QAI reflects the status of gender mainstreaming based on the contents of implementation documents, which vary considerably in their quality

and level of detail and do not always capture the real situation in the field. It must also be emphasized that this study did not review equal numbers of projects for each region because the size of the agriculture portfolio varies by region. Nevertheless, the QAI tool gives a general picture of gender mainstreaming and its regional variation in the agriculture project portfolio. A final consideration is that the tool cannot track the actual impacts of gender-responsive actions, which can be measured only after implementation is complete.

SAMPLE SELECTION

If the entire portfolio cannot be reviewed, a representative sample of projects from different regions can be selected based on previously defined criteria. For this review, projects were selected proportionally from the six regions based on whether the project was approved in or after FY08, when the three gender dimensions became mandatory for project preparation in agriculture. On that basis, 55⁷ of 236 active projects were selected for the review, which represented 26.45 percent of the net commitment of the agriculture portfolio (approximately \$5.53 billion) (appendix B). A qualitative review of a randomly selected sample of 14 ICRs (for projects completed between FY06 and FY13; see appendix B) was done to complete the analysis for the entire project cycle.

DOCUMENTS REVIEWED

The main operational documents for each project were reviewed—specifically, the Aide-Mémoires, Implementation Status and Results Reports, and Project Implementation/Operations Manuals (table 2.1). PIMs are considered government documents rather than World Bank documents, yet they provide considerable detail on the key implementation processes and activities; therefore, they

were particularly important to include in the review. To gain information about gender mainstreaming that may not have been captured by the documents just mentioned, the review team added a qualitative component, interviewing some of the TTLs (via e-mail or phone) about whether a project had any special studies, case studies, evaluations, and lessons learned in relation to gender.

SCORING PROJECTS

A choice was made to score the projects more rigorously for quality during implementation (QAI) than at entry (QAE), because *actual occurrences on the ground* are being scored, and each dimension does not carry equal weight.

The QAI methodology weighs gender actions more heavily than the other two gender dimensions because actions are the centerpiece of implementation; in addition, successful outcomes are sometimes achieved even without conducting a gender analysis or using a gender-sensitive M&E framework. It is important to keep in mind that conducting gender analysis and assessment of issues is crucial during implementation, as new gender issues that were absent or escaped attention in the design phase can arise. Gender analysis, monitoring, and evaluation during implementation can generate a holistic view of expected gender results, raise gender concerns, and assist with crafting well-informed, targeted gender actions.

Projects are scored within each gender dimension according to a binary scale that takes a value of 1 if the assessment is positive and 0 if it is not. Guiding questions are used to assess each gender dimension. Gender actions and gender M&E each require a positive answer to two guiding questions to achieve a value of 1. Overall, projects are rated Gender Implemented if they score at least 2 points, one of them being for gender actions (table 2.2).

⁷The sample included 13 projects for AFR, 9 for EAP, 8 for ECA, 9 for LAC, 4 for MNA, and 12 for SAR. The choice of projects for MNA was constrained by the limited number of active projects as well as projects rated for the three gender dimensions. All of the selected projects have almost two years of implementation and have started disbursing.

TABLE 2.1. GENDER IN IMPLEMENTATION: DOCUMENTS REVIEWED

Gender Dimension	Documents Reviewed	Rationale
Gender analysis	• Additional environmental or social assessments with a gender component.^a • Specific topic assessments related to gender issues that are associated with the project components. • General gender studies that could be used to inform the project.	• Additional gender analysis by theme or component helps to identify issues and define gender-specific activities during implementation.
Gender actions	• Aide-Mémoires • Midterm review reports • Project Implementation/Operations Manuals • Implementation Status and Results Reports • Project annual reports	• AMs record ongoing gender activities under the project, results achieved so far, issues identified, and next steps and recommendations to address issues. They note how World Bank teams track this process as implemented by the government and the Project Coordination/Implementation Unit. • Project Implementation/Operations Manuals translate projects into a series of actions and state the rules of operation. Gender inclusion is a key action for gender mainstreaming.
Gender-sensitive monitoring and evaluation	• Results frameworks in Implementation Status and Results Reports^b • Aide-Mémoires • Case studies • Specific evaluations • Project annual reports • Midterm review reports • Project Implementation/Operations Manuals	• The results framework shows how gender outcomes are tracked.

Source: Authors.

^a After the identification phase. Note that these documents often are not logged in the World Bank system; when they are not mentioned in AMs or MTRs, they must be supplied by the TTLs.

^b If the project started implementation recently and no indicator value is reported yet, the guiding question will focus only on the gender disaggregation of the indicator.

TABLE 2.2. GENDER IN IMPLEMENTATION AND COMPLETION: CHECKLIST FOR RATING PROJECTS

Gender in Implementation and Completion				
Gender Dimension	Criteria for Rating Project	Guiding Questions	Check	Score
Gender analysis	Gender analysis is incorporated in project manual(s), or further analysis on gender-related issues is conducted.	• Was any gender analysis conducted (for example, studies, social and environmental assessments, a substantive gender component of a study)?		1/0
Gender actions	Actions are taken to narrow gender disparities and to address the distinct needs of women/girls (men/boys) or to have positive impact(s) on gender equality.	• Are actions to incorporate gender mainstreaming outlined in project manual(s)? • Are World Bank recommendations made to the government to mainstream gender? • Did activities to mainstream gender occur?		1/0

If 2 boxes are ticked under gender actions, a score of 1 is achieved.

(Continued)

TABLE 2.2. GENDER IN IMPLEMENTATION AND COMPLETION: CHECKLIST FOR RATING PROJECTS (*Continued*)

Gender in Implementation and Completion				
Gender Dimension	Criteria for Rating Project	Guiding Questions	Check	Score
Gender monitoring and evaluation	Mechanisms to monitor and evaluate gender outputs and outcomes are functional.	• Is the core compulsory gender indicator in the results framework? • Are additional gender-disaggregated indicators in the results framework? • Were additional gender data collected and reported?		1/0 If 2 boxes are ticked under gender M&E, a score of 1 is achieved.
Overall score at implementation	Number of 1s in gender dimensions			1–3
Gender implemented	• Project must score at least 2 points, one of them being gender actions, to be rated Gender Implemented		Y/N	
Qualitative review of implementation (potential source documents in parentheses)	• Did the team include a gender specialist (World Bank/donor/government/other)? (AM) • What types of gender actions were taken? (AM, PIM) • To what extent is gender disaggregated in the results framework? (ISR) • Were any gender issues brought to the attention of government? (ISR, AM) • Were any gender issues brought to the attention of World Bank management? (ISR, AM) • What kind of gender-related operational measures were included in the PIM?			
Completion (Project Implementation and Completion report)	How successfully was gender mainstreamed in the project from entry to completion? • How was gender addressed? • Were gender activities successful? • What lessons were learned from gender mainstreaming?			

Source: Authors.

Note: AM = Aide-Mémoire, ISR = Implementation Status Report; ICR = Implementation Completion Report; and PIM = Project Implementation/Operations Manual.

CHAPTER THREE

FINDINGS OF THE GENDER IN IMPLEMENTATION REVIEW

This review is informative with respect to general trends and issues in gender implementation in the agriculture portfolio, but as discussed, the results should be treated with caution. The sample size is limited; without standardized and in-depth reporting on gender activities, it is impossible to fully gauge the quality of gender mainstreaming or of reporting on gender in projects that are rated Gender Implemented. A review of the entire agriculture portfolio would provide stronger evidence and yield valuable conclusions on gender in project implementation. Even so, the overview provided here, and the insights it offers into emerging trends and regional variation in gender mainstreaming, represents a useful starting point for examining gender in implementation. The gender actions documented from the implementation documents and TTL interviews fall into the eight categories shown in table 3.1.

RESULTS OF THE GENDER IN IMPLEMENTATION REVIEW BY REGION

On average, 76 percent of the projects were rated Gender Implemented based on the QAI review. All projects were Gender Implemented in MNA, compared with 89 percent in EAP; 85 percent in AFR; 75 percent in ECA and SAR; and 44 percent in LAC (figure 3.1).


As members of supervision teams, gender specialists played a crucial role in ensuring gender mainstreaming during implementation. Nearly all—94 percent—of the projects that had a gender specialist on the team were rated Gender Implemented. Different types of gender expertise were deployed from a variety of sources, such as World Bank gender specialists, consultants from other international institutions or donors (such as the Food and Agriculture Organization), and government gender specialists. In the most successful cases, both local and international gender specialists worked together. *This finding suggests that allocating project resources to engage a gender specialist can ensure gender implementation.*

TABLE 3.1. GENDER MAINSTREAMING IN IMPLEMENTATION: EXAMPLES OF GENDER ACTIONS

Activity Type	Examples of Gender Actions
Additional funds	• Assign a percentage of project funds for gender mainstreaming • Receive funds from other donors to fund gender-specific activities not originally planned for the project • Allot special funding (a “women’s revolving fund” or “women’s development fund”) to support creative ideas for designing and implementing activities targeting women and/or projects and activities run by women
Common sense: context-specific	• Keep training close to the home; provide bicycles • Conduct training in local languages that are mostly spoken by women • Provide day care during training • Recruit women trainers in the required technical field • Introduce labor-saving technologies
Expertise	• Recruit gender experts to assist the World Bank project team • Recruit gender experts in the Project Coordination/Implementation Unit (at national and regional level) • Get support for the project from government gender experts
Institutional engagement/ capacity building	• Incorporate existing women’s institutions (women’s unions, cooperatives, NGOs, and so forth) into the project to advance the gender agenda • Foster compliance with existing gender laws • Create gender units in ministries • Develop a gender strategy for the agriculture ministry • Support gender-sensitive policies • Establish a gender working group encompassing key players • Develop a gender strategy for the project/country/theme • Train government staff in gender issues/gender tools
Monitoring and evaluation; knowledge	• Develop specific mixed-method indicators to track gender • Regularly capture gender-related data along the results chain for each project subcomponent • Conduct gender-specific impact evaluation or impact evaluation with a gender component • Use diagnostics, thematic studies to recognize gender-specific constraints or opportunities, and design corresponding activities • Conduct specific case studies, qualitative studies; collect lessons learned on gender • Survey women regarding their satisfaction with specific activities/aspects of the project (usually via a questionnaire administered within a more general satisfaction questionnaire for beneficiaries) once specific activities are completed (planning, investments finalized, and so on) • Compile women’s success stories and best practices for dissemination
Project Implementation Unit: capacity	• Implement gender-sensitive hiring policies for staff and contractors • Train staff in gender issues and tools • Develop a gender-mainstreaming plan • Ensure that terms of reference for staff are gender sensitive • Ensure that Project Implementation Manuals mainstream gender • Ensure that the project’s communication strategy includes gender
Quotas/targets	• Set quotas of women beneficiaries by project activity and/or component • Set the percentage of women required in any type of committee • Define the number of women in leadership/decision-making roles (not only treasurer) in every committee • Encourage equal participation in project components and activities
Technical assistance; community capacity building	• Offer technical assistance to address gender-specific needs and capacity-building gaps • Ensure presence of female extension officers, paralegals, and other technical staff • Provide training in rights and sensitization to gender issues • Hold knowledge exchange workshops • Undertake campaigns on gender inclusion and issues • Conduct knowledge exchange visits among women’s groups

Source: Authors.


FIGURE 3.1. PROJECTS RATED GENDER IMPLEMENTED, BY REGION

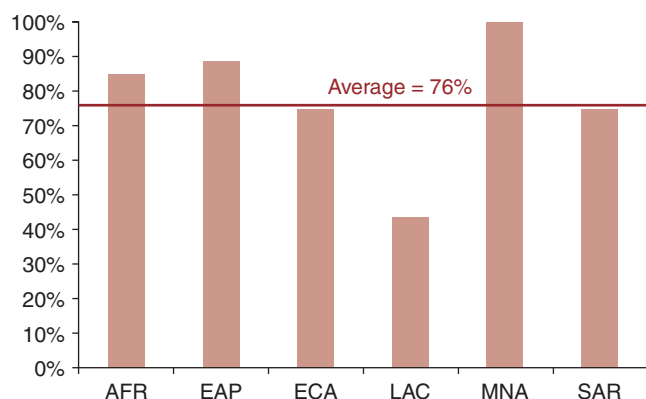

Source: Authors.

Note: AFR = Africa Region; EAP = East Asia and Pacific; ECA = Europe and Central Asia; LAC = Latin America and Caribbean; MNA = Middle East and North Africa; SAR = South Asia Region.

FIGURE 3.2. GENDER INFORMED AND GENDER IMPLEMENTED PROJECTS, BY REGION

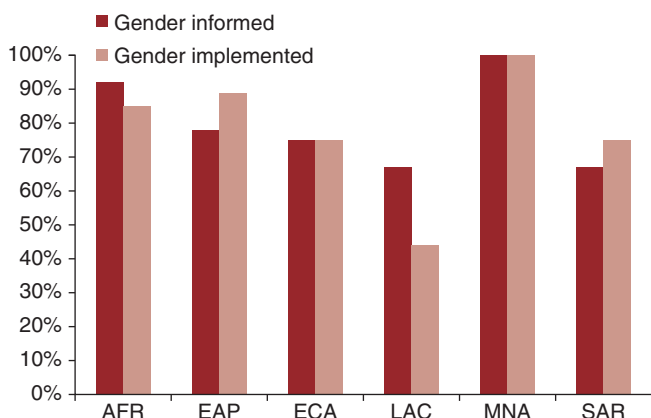


Source: Authors.

Note: AFR = Africa Region; EAP = East Asia and Pacific; ECA = Europe and Central Asia; LAC = Latin America and Caribbean; MNA = Middle East and North Africa; SAR = South Asia Region.

RESULTS BY GENDER INFORMED VERSUS GENDER IMPLEMENTED RATING


A project that takes gender into account during the design phase is not necessarily successful in integrating gender in implementation. At entry, 78 percent of projects were rated Gender Informed, compared to 76 percent that were rated Gender Implemented under this review. Among the projects rated Gender Informed at entry, 43 percent failed to meet the criteria for gender in implementation (figure 3.2). *Nevertheless, the review indicates that even if a project neglects gender during the*

FIGURE 3.3. PERCENTAGE OF PROJECTS BY GENDER INFORMED/ GENDER IMPLEMENTED CATEGORY

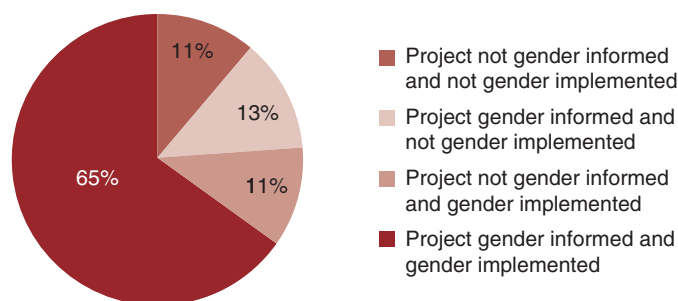

Source: Authors.

FIGURE 3.4. PERCENTAGE OF PROJECTS BY GENDER INFORMED/ GENDER IMPLEMENTED CATEGORY AND REGION




Source: Authors.

Note: AFR = Africa Region; EAP = East Asia and Pacific; ECA = Europe and Central Asia; LAC = Latin America and Caribbean; MNA = Middle East and North Africa; SAR = South Asia Region.

design phase, it may be possible to catch up during implementation, which did happen in 11 percent of the projects.

In spite of the World Bank's policy commitments, 11 percent of projects were neither Gender Informed nor Gender Implemented, with much variation across regions (figure 3.3 and figure 3.4).

FIGURE 3.5. PROJECTS CONDUCTING GENDER ANALYSIS AT IMPLEMENTATION

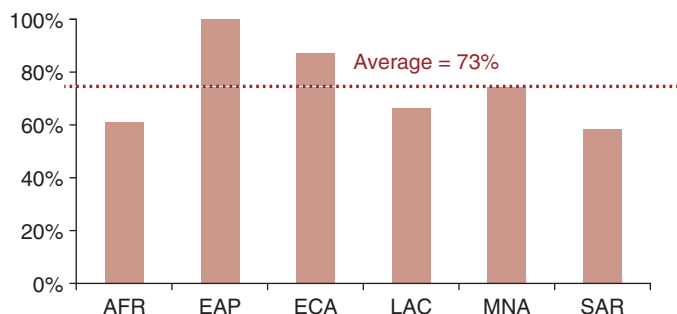

Source: Authors.

Note: AFR = Africa Region; EAP = East Asia and Pacific; ECA = Europe and Central Asia; LAC = Latin America and Caribbean; MNA = Middle East and North Africa; SAR = South Asia Region.

This result indicates that the commitments on gender mainstreaming have not been fully realized.

RESULTS BY GENDER DIMENSION


GENDER ANALYSIS

On average, 73 percent of projects conducted gender analysis in the implementation phase (figure 3.5). Conducting gender analysis during implementation is a substantially different exercise from gender analysis at entry. *Gender analysis during implementation often uncovers issues or concerns that arise as projects get under way or that were not captured at the design phase and are worthy of further research and assessment.* The analysis can also be thematic, focusing on specific project issues and components. Useful gender analyses at the implementation stage were also found in some PIMs and AMs.

Gender analysis conducted during implementation is likely to lead to gender actions. Among the projects that included gender activities,⁸ 80 percent had performed a gender analysis during implementation. However, gender analysis did not always lead to gender actions; 70 percent of projects with no gender actions had benefited from gender analysis during implementation (figure 3.6 and figure 3.7).

⁸ A gender action is an activity undertaken to mainstream gender during a project's implementation. Gender actions are identified in the QAI review by answering question 3 in the "Gender Actions" section (see table 3.1).


FIGURE 3.6. RELATIONSHIP BETWEEN GENDER ANALYSIS AND GENDER ACTIONS DURING PROJECT IMPLEMENTATION, BY REGION

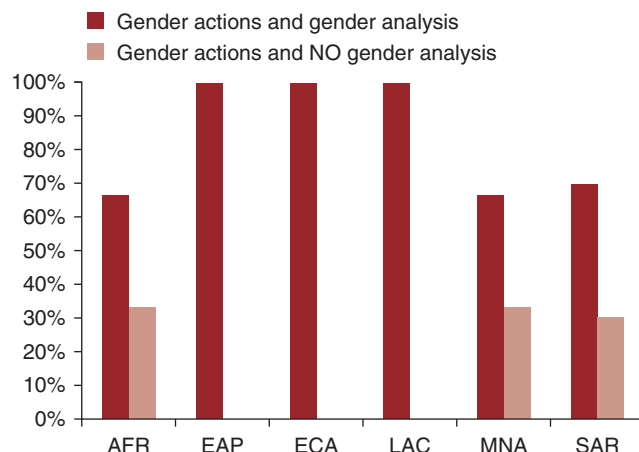

Source: Authors.

Note: AFR = Africa Region; EAP = East Asia and Pacific; ECA = Europe and Central Asia; LAC = Latin America and Caribbean; MNA = Middle East and North Africa; SAR = South Asia Region.

FIGURE 3.7. CHARACTERISTICS OF PROJECTS WITH NO GENDER ACTIVITIES, BY REGION

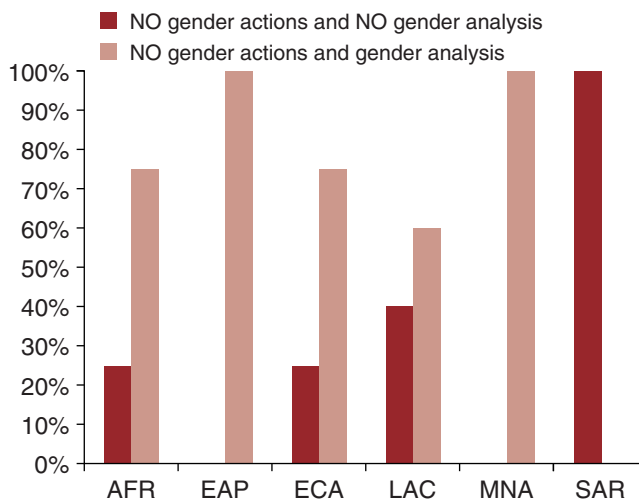


Source: Authors.

Note: AFR = Africa Region; EAP = East Asia and Pacific; ECA = Europe and Central Asia; LAC = Latin America and Caribbean; MNA = Middle East and North Africa; SAR = South Asia Region.

GENDER ACTIONS

The review of gender actions was based on three main questions (see table 2.2). First, does the PIM outline actions to incorporate gender mainstreaming? Second, does the World Bank make recommendations to the government

FIGURE 3.8. PROJECTS THAT SCORED 1 ON THE GENDER ACTIONS DIMENSION, BY REGION



Source: Authors.

Note: AFR = Africa Region; EAP = East Asia and Pacific; ECA = Europe and Central Asia; LAC = Latin America and Caribbean; MNA = Middle East and North Africa; SAR = South Asia Region.


to mainstream gender? Third, have activities to mainstream gender occurred? The analysis focused more on the third question, as it is the most critical element for achieving real gender outcomes. However, recall that two of the three guiding questions must have a positive answer for the gender actions dimension to receive a score of 1.

Gender actions were included in 69 percent of projects, with differences in performance across regions (figure 3.8). In 56 percent of the projects reviewed, the PIM outlined actions to mainstream gender (question 1).⁹ In 71 percent of the projects reviewed, the AMs included World Bank recommendations for the government to mainstream gender (question 2).

Activities to mainstream gender (question 3) occurred in 64 percent of the projects reviewed. If a project does not implement concrete gender actions, it is unlikely to achieve positive outcomes for women, regardless of whether the project conducted a gender analysis or had a gender-sensitive M&E system (figure 3.9). What is less clear from this review, however, is how effective the projects' gender activities really were and to what extent they were implemented. *This finding suggests that the World Bank needs a better reporting system for gender actions and a strengthened gender skills base.*

⁹ Out of the 55 projects, 43 PIMs were reviewed, as 12 PIMs were not provided by TTLs.

FIGURE 3.9. GENDER ACTIONS, BY REGION

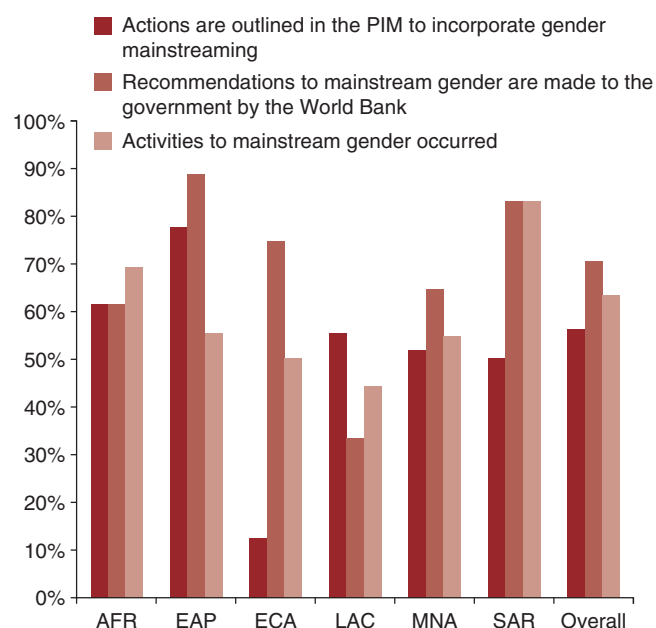


Source: Authors.

Note: AFR = Africa Region; EAP = East Asia and Pacific; ECA = Europe and Central Asia; LAC = Latin America and Caribbean; MNA = Middle East and North Africa; SAR = South Asia Region.

The quality and quantity of gender recommendations recorded in AMs, gender actions incorporated in PIMs, and activities to mainstream gender varied greatly across the group of projects that attained a score of 1 for the gender actions dimension:

1. Some PIMs treat gender issues in a vague, general manner. They mention the need to address them but specify no concrete actions and offer only generic recommendations. Other PIMs mainstream gender in the project's components and subcomponents and define concrete steps and actions that will be implemented.
2. Some AMs include a simple statement underlining that women are not benefiting from the project's activities but provide no concrete recommendations to address these observations. Other AMs identify progress and issues occurring in all project components and provide specific actions and recommendations to the government in an action matrix.
3. Activities to mainstream gender range from implementing one simple action (such as a quota for

FIGURE 3.10. DISTRIBUTION OF PROJECTS THAT DID/DID NOT MENTION ACTIONS TO MAINSTREAM GENDER IN PROJECT DOCUMENTS

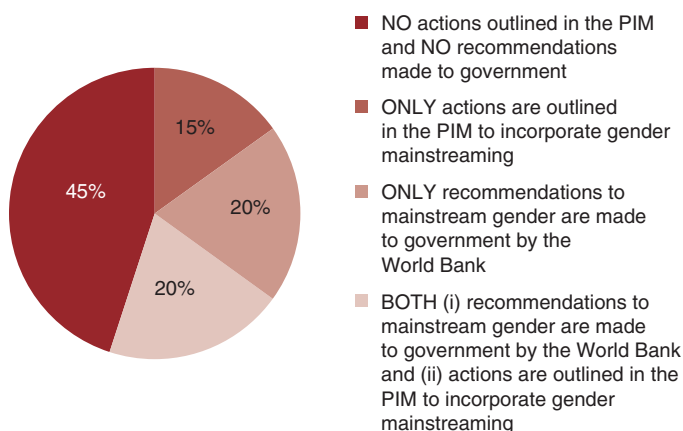

Source: Authors.

women to participate in a specific project activity) to mainstreaming a broad set of gender activities in all components of a project (see table 3.1). This creates a real synergy for gender mainstreaming and significantly increases the possibility of positive outcomes for women in the project.


The majority of projects (60 percent) that implemented gender actions specified those in the PIM and presented gender recommendations in the AMs. Only 3 percent of the projects that implemented actions to mainstream gender had specified no actions in the PIM and made no recommendations in the AMs.

In 45 percent of the projects, gender activities did not occur if they were not included in the PIMs or AMs. Another 20 percent of the projects without gender activities made gender recommendations in the AMs; 15 percent without gender activities only outlined gender actions in the PIM (figure 3.10).

GENDER MONITORING AND EVALUATION

The two main procedures specified by the World Bank to report on projects' gender achievements (the core compulsory gender indicator and gender-disaggregated data in the results framework) are not implemented extensively. The core

FIGURE 3.11. PROJECTS THAT SCORED 1 ON THE GENDER M&E DIMENSION, BY REGION



Source: Authors.


Note: AFR = Africa Region; EAP = East Asia and Pacific; ECA = Europe and Central Asia; LAC = Latin America and Caribbean; MNA = Middle East and North Africa; SAR = South Asia Region.

compulsory gender indicator—"Direct project beneficiaries (number), of which female (percentage)"—was monitored only by 42 percent of the projects reviewed. This finding is surprising, because these reporting procedures are required for investment projects approved as of July 1, 2009, and for projects that were formally restructured as of July 1, 2009 (see "Core Sector Indicators and Definition," August 2012¹⁰). Just 58 percent of the projects selected for review had disaggregated data by gender in the results framework; in most cases, the data were for core sector indicators that required data to be disaggregated by gender. **The gender M&E dimension is addressed in 60 percent of projects, with some variation across regions.** Two regions scored below 50 percent for gender M&E. Other regions scored quite high. All projects in MNA addressed gender in M&E; 88 percent did so in ECA, and 69 percent in AFR (figure 3.11).

Overall, only 20 percent of projects implement all three of the gender M&E activities. Forty percent of projects implemented none or one (figure 3.12). The scope and the quality of gender M&E data varied.

¹⁰ The results could have been affected by the fact that some projects from the sample were approved in 2008 (SAR, 5 projects; LAC, 1 project; ECA, 1 project; EAP, 2 projects; and AFR, 2 projects), but the impact of the approval date should be limited.

FIGURE 3.12. GENDER M&E ACTIVITIES, BY REGION

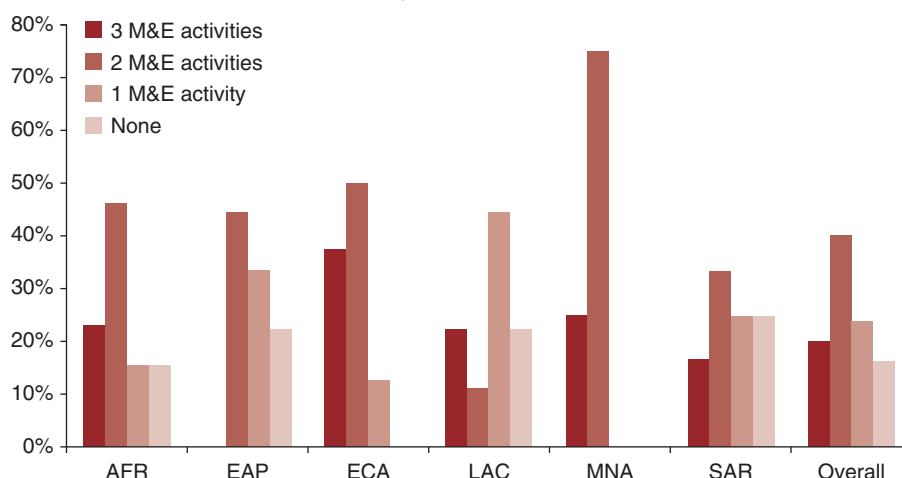

Source: Authors.

Note: AFR = Africa Region; EAP = East Asia and Pacific; ECA = Europe and Central Asia; LAC = Latin America and Caribbean; MNA = Middle East and North Africa; SAR = South Asia Region.

Some projects gave minimum consideration to gender issues in the M&E system; for example, the results framework used one single indicator, disaggregated by gender, to track female beneficiaries (most likely one of the core indicators from the Agriculture Global Practice); no other gender-sensitive indicators were included in the results chain. *These practices make it very difficult to track progress in gender issues during implementation and even to identify achievements related to gender when a project has ended.* At the other end of the spectrum, some projects developed a comprehensive M&E system that fully integrated gender by collecting gender-disaggregated data at the output, sub-outcome, outcome, and impact levels (sometimes supported by impact evaluations); they also collected essential qualitative data through focus groups, case studies, and other similar methods.

A concern emerging from this review is that the results frameworks were weak in the numbers of indicators that were (or could have been) disaggregated by gender and in the number and quality of indicators specifically designed to track outcomes for women. Results frameworks generally had a limited number of gender-disaggregated indicators, either because the project simply did not collect such data or because of the indicators that were chosen (some could not be disaggregated, whereas others focused on processes and institution-building rather than on outcomes and impacts on beneficiaries). In other words, *the choice of*

indicators for the results framework can preclude the possibility of disaggregating the data and thus prevent gender outcomes from being tracked.

Very few projects had specifically tailored indicators to track particular gender outcomes—for example, the percentage of research funds allocated to develop gender-sensitive technologies. It is clear that gender mainstreaming requires much more rigorous treatment in results frameworks to adequately track gender progress and achievements.

Overall, the most frequent gender M&E action undertaken by projects is “collecting and reporting on additional gender data” beyond the results framework (64 percent). Quantitative and qualitative data on outcomes for women were collected through evaluations, focus group discussions, case studies, and specific analyses to improve gender mainstreaming and/or scale-up of a successful effort to mainstream gender. It is extremely positive that so many projects collected data beyond the scope of the results framework. It is unfortunate that *this wealth of information on gender is not always captured within the World Bank’s regular reporting system (results framework); consequently, some of the Bank’s gender achievements are underreported, and valuable lessons are lost.*

The use of a compulsory core gender indicator (percentage of female beneficiaries) and even the

development of a robust results framework with gender-disaggregated data are not sufficient to implement gender, in particular with respect to the M&E system. The compulsory core gender indicator has limited usefulness for tracking progress in gender, provides no information on the type and quality of the benefits that a project provides to women, and quite frequently is measured poorly. The results framework provides an incomplete picture of gender achievements and progress. At midterm, some projects realize that they have been performing poorly in terms of gender because they have developed no other indicators outside the results framework and have collected no qualitative data. *The results framework is a critical tool for tracking project outcomes, but it is important to go beyond the results framework to capture project benefits more fully and in a deeper sense.*

Gender mainstreaming requires a robust M&E system that deploys diverse tools (for example, quantitative and qualitative studies, monitoring of outputs, processes, and outcomes, case studies, stakeholder interviews) to monitor and assess gender progress and achievements, both quantitatively and qualitatively, during implementation. Gender mainstreaming also implies the development of *gender-sensitive indicators along the entire results chain*, from input to output to outcome and finally to impact. An M&E system using such diverse tools and collecting a variety of data on gender asymmetries is able to generate a comprehensive set of data to understand and evaluate gender outcomes. Such diagnostic data can be used to identify gender impediments during implementation and form a basis to craft well-informed solutions that can be implemented before the project closes.

GENDER TRACKING OF IMPLEMENTATION AND COMPLETION REPORTS

Of all the documents reviewed, the ICRs had the greatest wealth of gender data, because they include a designated section for reporting on gender. This implies that simply including gender sections in World Bank documents would facilitate more accurate reporting on progress and achievements in mainstreaming gender; it would also allow projects to incorporate the resulting lessons as the project cycle proceeds and adjust activities

accordingly. *This finding also suggests that projects may implement more gender activities than they actually report.*

ICRs are clearly a valuable tool for gender learning, and the data they contain on gender should be reviewed on a regular basis. A close qualitative analysis of the types of gender outcomes recorded in ICRs can give insights into how gender is mainstreamed in World Bank projects. Many projects used the familiar roster of tried-and-true gender activities that were listed in table 3.1—training, participatory processes, and targets, to mention a few. It was clear from the ICRs that these actions do not always work in every context. They must be monitored and revised where necessary—hence the *need for better gender reporting during the project cycle.*

Not all ICRs excelled in reporting on gender. Some were still very poor, adding to the underreporting of gender results and outcomes and causing opportunities to be missed during implementation.

GENDER CONTENT IN THE KEY DOCUMENTS REVIEWED

AIDE-MÉMOIRE

The AM is a critical World Bank document for reporting on gender in projects. It reports on gender activities conducted under a project, the gender results achieved so far, the gender issues identified, and the next steps and recommendations to address those issues. The AM is developed jointly with the borrower during the implementation and supervision mission.

As might be expected, the AMs reviewed here varied in quality. Some were completely gender neutral, whereas others included detailed, action-oriented checklists. Two good practices identified through this review are gender-specific sections and component-based gender mainstreaming. The AM has no template or required format. The interests of the TTLs and other project team members determine the extent to which AMs address gender issues or actions. *The participation of a gender specialist in supervision missions is one way to ensure that gender concerns are taken on board and monitored closely throughout implementation. However, in the long term, a more sustainable and efficient solution is for World Bank sector staff to build general capacity for gender in*

implementation teams, leaving the more narrow technical and social topics to the gender specialists.

In a robust AM, gender is assessed across components (subcomponents) or through a specific gender section and detailed annex. It discusses gender-related activities, documents progress, identifies gender-related issues, and records the specific follow-up actions and recommendations agreed to by the government. The AM for Zambia's Irrigation Development and Support Project (IDSP) lists agreed gender actions in a table; this is a good example of a concise gender action matrix (appendix A).

IMPLEMENTATION STATUS AND RESULTS REPORT

The ISR provides a picture of the World Bank's internal reporting on gender activities, issues, results, and follow-up actions. The content of an ISR is updated twice each year and is mostly informed by AMs from previous missions. This review looked at ISRs mainly to assess the results framework indicators and the core gender indicator.

It is important to note that the ISR has no designated section or specific requirements for reporting on gender. When gender is included, usually it is in the form of a report on disaggregated core sector indicators, but gender activities, issues, and actions are rarely discussed. *The overall picture emerging from this review is that the ISR, in its current form, is not very useful for helping to understand*

whether any gender activities took place in a project, to capture gender issues, or to document gender achievements.

PROJECT IMPLEMENTATION/ OPERATIONS MANUAL

The PIM is a particularly important document because it details the key processes and activities that define how a project will be implemented.

PIMs specify how gender implementation will occur, while considering the institutional capacity for integrating gender into project activities. The review of PIMs for the selected projects reveals the number and quality of processes and actions developed to ensure that gender is addressed during implementation. As the PIM is a living document, it is updated during implementation as the need arises, offering multiple opportunities to further strengthen gender mainstreaming during implementation.

A high number of PIMs outline activities to mainstream gender, but the scope, quality, and quantity of those actions varies greatly from project to project, even among the projects rated Gender Implemented.¹¹ Some project manuals have the bare minimum of gender processes and activities. They observe that women should be included in and benefit from the project's activities, but they do not lay out concrete actions to achieve this within the components and subcomponents of the project. But there were also outstanding PIMs, which describe concrete gender actions for most subcomponents of the project.

¹¹ Out of the 55 projects, 43 PIMs were reviewed, as 12 PIMs were not provided by TTLs.

CHAPTER FOUR

GENDER IMPLEMENTED: BASELINE AND TARGETS

The Agriculture Global Practice recognizes that the implementation of gender mainstreaming is important for a project's success. This review makes it possible to establish a baseline and to suggest a set of targets for a long-term approach to gender mainstreaming in agriculture projects. In particular, the focus on all three gender dimensions during implementation will raise the bar in terms of the quality of implementation.

According to the Agriculture Action Plan 2013–15, which sets the Quality at Entry parameters for agriculture and rural development projects, by 2015 projects will (1) include gender analysis in project design, with a target of 100 percent, and (2) include gender mainstreaming in all three dimensions of design (analysis, actions, and M&E), with a target of 75 percent. The 100 percent target for gender analysis reflects the fact that all projects should be assessed to identify any gender asymmetries related to the chosen interventions and understand their potential implications. Even if it is deemed unnecessary to include gender in the design, that decision needs to be based on a sound gender analysis.

Based on the Quality at Entry targets, senior management could consider setting similar gender mainstreaming targets for Quality at Implementation, as suggested in table 4.1.

TABLE 4.1. SUGGESTED GENDER IMPLEMENTED TARGETS

	Baseline	Target			
		FY15	FY16	FY17	FY18
Gender implemented					
Projects reviewed rated Gender Implemented	76%	80%	85%	90%	95%
Gender dimensions (1 = yes; 0 = no)					
Gender analysis rated 1	73%	80%	85%	90%	95%
Gender actions rated 1	69%	80%	85%	90%	95%
Gender M&E rated 1	60%	80%	85%	90%	95%

Source: Authors.

CHAPTER FIVE

CONCLUSIONS AND DISCUSSION

There is much to celebrate in this tracking exercise. A promising number of agriculture projects across regions were rated Gender Implemented. This data could not have been generated without the QAI tool; this tool was effective for gathering information on gender mainstreaming reported in implementation documents and for clearly identifying gaps and strengths for specific projects and gender trends in regional portfolios.

There is a need to move beyond quality at entry to have a more realistic picture of gender mainstreaming in projects. This review indicates that a rating of Gender Informed at entry is no guarantee that a project will successfully mainstream gender during implementation, although it is a good basis for success. In addition, this review shows that it is critical to track gender mainstreaming throughout the project cycle to identify gaps and opportunities in real time. Finally, the review shows that if a project neglects gender during the design phase, it can still catch up during implementation.

Gender mainstreaming can involve several activities and approaches, including affirmative actions to actively promote women's inclusion and empowerment on the ground. The gender actions in the reviewed documents (see table 3.1) resemble affirmative actions and others that are predominantly directed at mainstreaming gender in projects. Clearly different types of actions are needed to actively promote women's empowerment on the ground, fitting to specific contexts. A substantial number of gender actions do *not* require additional project funding. Instead of additional funding, what is needed is a change in management and implementation attitudes, as well as a change in the skills base recruited for project teams. In other words, the easy wins are there—if project teams apply a gender lens in project implementation.

The quality of gender mainstreaming varies. Some projects do the bare minimum by undertaking only a few concrete actions, including the minimum core sector indicators for gender (such as tracking the percentage of women beneficiaries), and potentially adding another gender-disaggregated indicator. Other projects go much farther in mainstreaming gender. They integrate gender actions within each

component and subcomponent and develop an M&E system that fully integrates gender (not only tracking numbers of women beneficiaries but also disaggregating most indicators by gender and developing gender-specific indicators). Some projects conduct additional analysis to further inform a strategy for mainstreaming gender and/or to scale up best practices, and some projects determine that they need to conduct a gender thematic study (such studies often are conducted to enhance the understanding of how specific gender practices can influence the achievement of project objectives).

The World Bank’s reporting requirements and document templates do not systematically incorporate gender. The formats for two key implementation documents—the AM and ISR—require no reporting on gender. Its inclusion is ad hoc, resulting in great variation in the quality of the Bank’s reporting on gender and likely a degree of underreporting. ICRs, which have a designated section for reviewing gender mainstreaming, report much more comprehensively on it. The main cause of underreporting simply seems to be that reporting is not required in the main implementation documents. This review reveals that a wealth of information on gender mainstreaming is not captured by the main implementation documents but can be found instead in other documents (case studies or evaluations).

The current guidelines, processes, and support for TTLs (human and financial resources) do not drive gender mainstreaming during implementation and completion. It is critical that all of the documents required for projects clearly define the expectations and requirements for reporting, monitoring, and addressing gender issues. These steps will contribute to improved gender outcomes and will facilitate the identification and documentation of lessons after a project ends.

There is a need to move beyond the results framework. Projects do not fully comply with the two main procedures for reporting on progress in gender—tracking the core compulsory gender indicator and incorporating gender-disaggregated indicators in the results framework. Nor is that information sufficient for truly knowing how effectively World Bank projects are addressing gender

issues. Gender mainstreaming requires a robust M&E system that deploys diverse tools (such as quantitative and qualitative evaluations, outcome monitoring, monitoring of outputs and processes, case studies, and impact evaluations) to monitor and assess gender progress and achievements during implementation.

Gender mainstreaming needs to be seen as technical skill, which requires resources. This review reveals that the key element of reaching a high score in gender implementation is the availability of gender expertise, in one form or another, during implementation. Good practices often arise from a mixture of task team members’ gender expertise, expertise within projects and from development partners, and local gender consultants. Qualified gender expertise correlates very strongly with success in gender implementation (particularly in the form of concrete gender actions and good practices) and with gender reporting. From this study, it is difficult to determine which comes first, the team’s overall awareness in gender issues and thus recruitment of gender expertise, or availability of special funds for gender inclusion and thus better gender implementation and reporting.

There is a set of limiting factors to gender mainstreaming. There was much to celebrate in this tracking exercise—a significant number of Agriculture Global Practice projects across regions were rated Gender Implemented—yet a subset of projects did not achieve that rating. Numerous factors limit gender mainstreaming. First, gender mainstreaming is still somewhat driven by the individuals present on the project team, resulting in great variation in the quality of gender mainstreaming. Second, no real data are available at the General Portfolio Management level to assess the quality of gender mainstreaming throughout the project portfolio. Third, financial resources to support gender mainstreaming in projects are very limited. Fourth, gender expertise and skills within the World Bank to support project teams are limited. Fifth, basic World Bank tools and documents do not encompass gender. Sixth, some project teams can perceive gender mainstreaming as an extra burden owing to the lack of time, financial resources, human resources, and more particularly guidance on the concrete steps and actions that a particular project should take to mainstream gender.

CHAPTER SIX

RECOMMENDATIONS

- 1. Overall, it is important to expand gender tracking throughout the project cycle.** Continued and deepened regular analyses of agriculture projects during the concept note stage, during the quality at entry steps (Quality Enhancement Reviews, Project Appraisal Documents), and during implementation, up to the ICR, where best practices can be identified, is proven to strengthen strategic gender implementation and outcomes. Harmonizing portfolio review methodologies at entry, implementation, and project closing improves our understanding of the consistency of gender mainstreaming in agriculture projects.
- 2. Use the Gender in Implementation tracking tool to identify gender gaps in order to provide proactive support to TTLs.** The tool can identify projects performing poorly on gender issues during implementation and can garner support for TTLs. It is suggested that a review of gender implementation in the agriculture portfolio be conducted every second year. The Gender Cross-Cutting Solution Area; the Urban, Rural, and Social Development Global Practice; and the Agriculture Global Practice are encouraged to regularly review Gender Informed (at design) and Gender Implemented scores and to agree on how to proactively support poorly performing projects. The methodology presented here can also be applied at the midterm of a project to quickly gain an understanding of the situation in a given project and change course, if needed, before the project closes.
- 3. Ensure gender skills, tools, and funding for each project.** For project staff, training in gender skills and concrete actions as well as in strategies for overcoming possible obstacles to gender implementation is essential. It is important to develop user-friendly tools for TTLs; for example, checklists to review progress on gender in implementation at the MTR stage, to monitor gender during implementation and to provide sample terms of reference for the recruitment of gender specialists. Furthermore, it is suggested that a pool of gender expertise could be established to provide resources for such support. However, the ultimate goal is for project and supervision budgets to allocate resources explicitly to support gender actions.

4. Management has a responsibility to take action on gaps in gender mainstreaming.

It is important to sensitize management and provide tools and guidance on how to review project documents (that is, Project Appraisal Documents, Aide-Mémoires, Implementation Status Reports, Implementation and Completion Reports) with a gender lens and suggest remedial action as needed. Such interaction between management and TTLs is also an opportunity to build commitment to monitor gender progress, and it has the potential to increase staff accountability to enhance gender mainstreaming. In addition, the Independent Evaluation Group (IEG) is well positioned to increase gender mainstreaming in implementation within the World Bank by consistently reviewing projects in terms of quality of gender in implementation and completion. It is suggested that IEG continues to emphasize gender as a thematic issue by systematically tracking how gender is addressed in projects and which results are achieved. Increasing the weight of gender mainstreaming in project ratings has the potential to incentivize TTLs to integrate gender in implementation. At the same time, task teams need to fully use the ICR to report on gender, using the dedicated field “Poverty, social, and gender impacts,” in addition to the matrix of indicators.

5. Improve gender reporting within the World Bank system. Encourage TTLs to report on gender in Aide-Mémoires. Systematized reporting will provide a better understanding of the real situation of gender mainstreaming and thus support reducing under- and overreporting. A potential revision of the Aide-Mémoire Guidelines for reporting progress on gender issues, actions, and recommendations to government could be accompanied with a short training session for users (for example, in the form of e-learning).

6. Secure a robust M&E system that deploys diverse tools, including quantitative and qualitative methods to assess gender issues, progress, and achievements. The M&E system of a project needs to develop gender-sensitive indicators along the entire results chain, to use a diverse set of tools, and to collect a variety of data to assess gender outcomes. At the same time, it is very important to learn from the impact evaluation studies being conducted by the Gender Innovation Lab (GIL) and others to increase the knowledge of what does and does not work. It is necessary to identify any gender-related impediments for project benefits throughout implementation, to investigate the issues, and to propose solutions so that these gender asymmetries can be removed or mitigated.

7. Systematize links between the World Bank’s gender experts. To generate positive synergies, it is essential to create working relationships among the World Bank’s gender experts from the Agriculture Global Practice; the Gender Cross-Cutting Solution Area; the Urban, Rural, and Social Development Global Practice; and the other global practices and CCSAs. Greater synergy would allow gender expertise to be engaged more broadly and for lessons and good practices to be shared and disseminated more widely within and across the regions and sectors.

8. The Agriculture Global Practice should set targets for gender implementation. Setting targets derived from the baseline established in this review can incentivize projects and regions to improve their performance and monitor progress against agreed targets. Unit and staff accountability for gender mainstreaming can be enhanced by such targets and can be one way to reach the desired development outcomes.

REFERENCES

- FAO (Food and Agriculture Organization). 2011. *The State of Food and Agriculture 2010–11. Women in Agriculture: Closing the Gender Gap for Development*. Rome: FAO.
- O’Sullivan, Michael; Rao, Arathi; Banerjee, Raka; Gulati, Kajal; Vinez, Margaux. 2014. *Levelling the Field: Improving Opportunities for Women Farmers in Africa*. Washington, DC: World Bank Group. <http://documents.worldbank.org/curated/en/2014/01/19243625/levelling-field-improving-opportunities-women-farmers-africa>.
- World Bank. 2011. *World Development Report 2012: Gender Equality and Development*. Washington, DC: World Bank.
- . 2013. *Special Themes for IDA17*. IDA17. Washington, DC: World Bank. <http://documents.worldbank.org/curated/en/2013/06/17885991/special-themes-ida17>.
- . Internal Paper. 2012. *Integrating Women Producers and Their Organizations into Agricultural Investment Programmes in Zambia and Mali*. Washington, DC: World Bank.
- . Internal Paper. 2013. *Women’s Land Ownership and Compensation Study in Zambia*. Washington, DC: World Bank.

APPENDIX A

GOOD PRACTICE EXAMPLES

Below is a sample of good practice documents that were reviewed during this activity, with an outline of the factors that made them successful for replication by other project teams.

IMPLEMENTATION AND STATUS RESULTS: BOLIVIA PROYECTO DE INVERSIÓN COMUNITARIA EN ÁREAS RURALES (PICAR) COMMUNITY INVESTMENT IN RURAL AREAS (P107137)

Gender features in all Implementation and Status Results documents. It is a requirement that all agriculture projects include in their results framework the core compulsory gender indicator on female beneficiaries. This indicator has been successfully included in the ISRs of this project. Moreover, the gender achievement of the project is also captured through the following proposed project development objective indicators:

- » Community (of which women's) subprojects that satisfactorily achieve 75 percent of expected results
- » Community (of which women's) subprojects fully functional one year after their completion

In addition, the proposed Intermediate Results Indicators are also intended to capture the project's impact on women:

- » Community members (of which women) having attended at least one training event
- » Beneficiary satisfaction (of which women)
- » Unqualified audits in women's subprojects
- » Community subprojects financed, of which women's subprojects

AIDE-MÉMOIRE: ZAMBIA IRRIGATION DEVELOPMENT AND SUPPORT PROJECT (IDSP) (P102459)

The inclusion of a specific gender section in the Aide-Mémoire is key in mainstreaming gender in implementation (table A.1). It allows close supervision of the activities undertaken toward the implementation of gender actions and follow-up during the next mission. Inclusion of a gender specialist in the team ensured that gender concerns were

TABLE A.1. ZAMBIA IRRIGATION DEVELOPMENT AND SUPPORT PROJECT AIDE-MÉMOIRE: AGREED GENDER ACTIONS (2011)

Actions	Responsibility	Deadline
Organize sensitization for chiefs and households on women's land ownership rights	Community mobilizers and MACO	December 2011 (start date)
Organize site-to-site exchange visits (women/men) to all sites to share experiences on women's land ownership rights	MACO and community mobilizers	January 2011
Involve household members, women and men, in the asset survey	MACO	November onward
Establish a quota of 50/50% women/men as WUA executive committee members	Community mobilizers/ MACO	November onward
Provide training for (young) women in leadership and PC skills	Community mobilizers	December onward
Conduct feasibility study to improve food processing and marketing for products produced by women	MACO	March 2012

Source: World Bank, IDSP Project Document.

Note: MACO = Ministry of Agriculture and Cooperatives; WUA = water user association.

taken on board and were closely monitored. In IDSP, a brief gender analysis and identification of gender roles was conducted, and the mission observed differences among the project sites in terms of women's needs, recognizing that gender mainstreaming is not a one-size-fits-all approach.

In this prime example of an Aide-Mémoire, many gender actions are included/recommended: setting quotas for women's participation in water user associations (WUAs); introducing training for leadership skills, targeting women and separate gender training (tools, methodology, analysis, and so on) for the project staff; including a gender-specific annex in quarterly reporting formats; and ensuring that TOR (baseline, MTR, and end of project evaluation) specifies that all data will be collected and analyzed in a sex-disaggregated form. All these are presented in an action matrix in the AM. This makes sure each activity targeting women is monitored closely and followed through.

TRAINING OF TRAINERS GUIDE: PHILIPPINES PARTICIPATORY IRRIGATION DEVELOPMENT PROJECT (PIDP) (P088296)

A manual was developed under the PIDP that aimed at mainstreaming gender concerns in all the activities of the National Irrigation Administration (NIA) and at increasing employees' awareness of women's concerns throughout the agency's operations. This facilitator's training manual details how to design and carry out a training program aimed at recognizing women's roles as "irrigation partners" and as "untapped resources," in addition

to them being beneficiaries of the project. This helped increase the NIA officers' and members' understanding of the different roles and needs of male and female farmers and led to an action plan for operationalizing gender in project implementation activities. By analyzing the legal framework and the importance of gender mainstreaming in irrigation, the training engaged the participants to discuss their understanding of gender relations in their community and in their irrigation association, which then informed subsequent actions.

GENDER-SPECIFIC STUDIES: ZAMBIA IRRIGATION DEVELOPMENT AND SUPPORT PROJECT (P102459)

Once gender concerns in a specific project have been identified, the preparation of a gender-specific study can help to illuminate gender constraints and make targeted recommendations for successful project implementation. This was the case in the Irrigation Development and Support Program (IDSP) in Zambia. Two interlinked gender-specific studies were prepared, one focusing on women's producer organizations and another on how women's right to land influences their interest and modality of participating in the project.

The process, findings, and recommendations of the first study are described in the report *Integrating Women Producers and Their Organizations into Agricultural Investment Programmes in Zambia and Mali*. (2012) The details of the land ownership study appear in the report *Women's Land Ownership and Compensation Study in Zambia* (2013).

APPENDIX B

TYPES OF DOCUMENTS REVIEWED

Aide-Mémoire: Aide-Mémoires provide (1) a detailed description of activities occurring under the project, (2) the results achieved so far, (3) issues identified, and (4) next steps to address issues. The main purpose of an AM is to record the major findings, issues, recommendations, and agreements or next steps reached jointly with the borrower during the implementation support visit. The AM is also used to inform World Bank management about the status of a given project. For that reason, a review of AMs makes it possible to track and assess how gender activities and issues are accommodated, included, and followed up with government during implementation from the World Bank side.

Implementation Status and Results Report: ISRs provide a picture of the World Bank's internal reporting on gender activities, issues, results, and follow-up actions.

Project Implementation/Operational Manual: PIMs detail how a project will be implemented, including the specific processes and activities involved. PIMs make it possible to assess which processes and activities have been developed to ensure that gender is addressed during a project's implementation.

Implementation Completion Report: ICRs provide (1) a complete and systematic account of the performance and results of each operation, (2) a means of capturing and disseminating experience gained from an operation's design and implementation, and (3) accountability and transparency. They also serve as a vehicle for realistic self-evaluation. A review of ICRs provides information on how projects have affected women and other data relating to women.

Results framework: The results framework focuses on the project development objective (PDO) and intermediate outcomes expected from implementing each component of a project, all of which contribute to the achievement of the PDO. The added emphasis on component outcomes helps to focus the project's design and management on results. Results frameworks provide information on how gender is being integrated into the design of projects to contribute to their main outcomes.

APPENDIX C

SAMPLE SELECTION OF PROJECTS

The sample of projects reviewed for this study was selected from the 236 active Agriculture and Environmental Services (AES) projects (62 from AFR, 46 from EAP, 30 from ECA, 40 from LAC, 8 from MNA, and 50 from SAR). Fifty-five projects were selected for review, based on the following criteria:

- » Projects reviewed at the preparation stage were included. All of the projects selected are from FY08 and later, as the three gender dimensions for preparing AES projects became mandatory only in FY08.
- » The projects were chosen proportionally from the six regions: 13 for AFR, 9 for EAP, 8 for ECA, 9 for LAC, 4 for MNA, and 12 for SAR. The choice of projects for MNA was constrained by the limited number of projects that were both active and rated for the three gender dimensions.
- » All of the selected projects had at least one year of implementation and had started disbursing.

TABLE C.1. AFRICA REGION PROJECT SAMPLE FOR REVIEW

Region and Country	Project	Project Number	Approval FY	Closure FY	Net Committed Amount (Loan Amount Minus Any Cancellation)
1 Africa	Eastern Africa Agricultural Productivity	P112688	2009	2015	120
2 Angola	Market Oriented Smallholder Agriculture	P093699	2009	2015	22
3 Democratic Republic of Congo	Agriculture Rehabilitation and Recovery Support	P092724	2010	2015	120
4 Ethiopia	Agricultural Growth Program	P113032	2011	2016	150
5 Kenya	Agricultural Productivity and Agribusiness Project	P109683	2009	2015	82
6 Malawi	Agricultural Development Program Support Project	P105256	2008	2015	62
7 Niger	Agro-Pastoral Export Promotion Project	P095210	2009	2014	40
8 Nigeria	Commercial Agriculture Development	P096648	2009	2015	150
9 Uganda	Preparedness and Control of Avian Influenza	P110207	2008	2014	10
10 Zambia	Irrigation Development and Support Project	P102459	2011	2018	115
11 Ethiopia	Pastoral Community Development II	P108932	2008	2014	80
12 Nigeria	Fadama Development-III SIL	P096572	2009	2018	450
13 Tanzania	Accelerated Food Security Project	P114291	2009	2014	185

Source: Authors.

Note: Figures in the Net Committed Amount column are in millions.

TABLE C.2. EAST ASIA AND PACIFIC REGION PROJECT SAMPLE FOR REVIEW

Country	Project	Project Number	Approval FY	Closure FY	Net Committed Amount (Loan Amount Minus Any Cancellation)
1 Papua New Guinea	Smallholder Agriculture Development	P079140	2008	2014	28
2 Vietnam	Mekong Delta Water Management for Rural Development	P113949	2011	2017	160
3 Vietnam	2nd Northern Mountains Poverty Reduction	P113493	2010	2015	150
4 Samoa	Agriculture Competitiveness Enhancement	P115351	2012	2017	8
5 Vietnam	Managing Natural Hazards Project	P118783	2013	2019	150
6 China	Sustainable Development in Poor Rural Areas	P099751	2010	2016	100
7 Vietnam	Land Administration Project	P096418	2008	2015	75
8 Philippines	Participatory Irrigation Development	P088926	2009	2015	70
9 Vietnam	Agriculture Competitiveness Project	P108885	2009	2014	60

Source: Authors.

Note: Figures in the Net Committed Amount column are in millions.

TABLE C.3. EUROPE AND CENTRAL ASIA REGION PROJECT SAMPLE FOR REVIEW

Country	Project	Project Number	Approval FY	Closure FY	Net Committed Amount (Loan Amount Minus Any Cancellation)
1 Kosovo	Agriculture and Rural Development Project	P112526	2011	2018	20
2 Uzbekistan	Rural Enterprise Support Project II	P109126	2008	2017	108
3 Bosnia and Herzegovina	Irrigation Development Project	P115954	2012	2018	40
4 Kosovo	Real Estate Cadastre Project	P101214	2010	2016	12
5 Azerbaijan	Water Users Association Project	P107617	2011	2016	80
6 Kazakhstan	Second Irrigation and Drainage Improvement Project	P086592	2013	2022	103
7 Kyrgyz Republic	Second Land and Real Estate Registration Project	P108178	2009	2014	6
8 Armenia	Community Agricultural Resource Management and Competitiveness Project	P120028	2011	2017	16

Source: Authors.

Note: Figures in the Net Committed Amount column are in millions.

TABLE C.4. LATIN AMERICA AND CARIBBEAN REGION PROJECT SAMPLE FOR REVIEW

Country	Project	Project Number	Approval FY	Closure FY	Net Committed Amount (Loan Amount Minus Any Cancellation)
1 Mexico	Sustainable Rural Development	P106261	2009	2017	100
2 Colombia	Second Rural Productive Partnerships	P104567	2008	2015	30
3 Brazil	Acre Social and Economic Inclusion and Sustainable Development Project—PROACRE	P107146	2009	2015	120
4 Bolivia	PICAR Community Investment in Rural Areas	P107137	2012	2017	40
5 Brazil	Pernambuco Rural Economic Inclusion	P120139	2012	2019	100
6 Haiti	Relaunching Agriculture: Strengthening Agriculture Public Services II Project (GAFSP-IDA)	P126744	2012	2017	40
7 Argentina	Second Provincial Agricultural Development	P106684	2009	2015	300
8 Jamaica	Rural Economic Development Initiative	P105122	2010	2017	15
9 Peru	Sierra Rural Development Project	P079165	2011	2016	40

Source: Authors.

Note: Figures in the Net Committed Amount column are in millions.

TABLE C.5. MIDDLE EAST AND NORTH AFRICA REGION PROJECT SAMPLE FOR REVIEW

Country	Project	Project Number	Approval FY	Closure FY	Net Committed Amount (Loan Amount Minus Any Cancellation)
1 Djibouti	Rural Community Development and Water Mobilization	P117355	2011	2017	9
2 Egypt, Arab Republic of	Farm-Level Irrigation Modernization	P117745	2011	2016	100
3 Tunisia	Second Natural Resources Management Project	P086660	2010	2016	36
4 Tunisia	4th Northwest Mountainous and Forested Areas Development Project	P119140	2011	2017	42

Source: Authors.

Note: Figures in the Net Committed Amount column are in millions.

TABLE C.6. SOUTH ASIA REGION PROJECT SAMPLE FOR REVIEW

Country	Project	Project Number	Approval FY	Closure FY	Net Committed Amount (Loan Amount Minus Any Cancellation)
1 Bangladesh	Water Management Improvement Project	P040712	2008	2015	94
2 Nepal	Irrigation and Water Resources Management Project	P099296	2008	2014	64
3 Nepal	Social Safety Nets Project	P113002	2009	2015	59
4 Pakistan	Sindh Water Sector Improvement Project	P084302	2008	2015	150
5 Afghanistan	National Solidarity Program III	P117103	2010	2016	40
6 Bangladesh	Social Investment Program Project II	P073886	2010	2016	115
7 India	National Rural Livelihoods Project	P104164	2012	2018	550
8 Sri Lanka	Second Community Development and Livelihood Improvement Project	P087145	2010	2014	75
9 Bangladesh	National Agricultural Technology Project	P084078	2008	2014	63
10 Nepal	Poverty Alleviation Fund II	P105860	2008	2018	245
11 India	Orissa Rural Livelihoods Project	P093478	2009	2015	82
12 Pakistan	Third Pakistan Poverty Alleviation Fund Project	P105075	2009	2015	250

Source: Authors.

Note: Figures in the Net Committed Amount column are in millions.

TABLE C.7. PROJECT SAMPLE SELECTION FOR REVIEWING IMPLEMENTATION COMPLETION REPORTS

Country	Title	Project Number	FY
1 Ethiopia	Capacity Building for Agricultural Services	P079275	2012
2 Kenya	Arid Lands Resource Management Project Phase Two	P078058	2011
3 China	Poor Rural Communities Development Project	P071094	2011
4 Lao PDR	Second Land Titling Project	P075006	2009
5 Turkey	Agricultural Reform Implementation Project (ARIP)	P070286	2009
6 Ukraine	Rural Land Titling and Cadastre	P035777	2013
7 Brazil	Land-Based Poverty Alleviation Project I	P050772	2009
8 Haiti	Haiti Community Driven Development (CDD) Project	P093640	2013
9 Iran	Alborz Integrated Land and Water Management	P071170	2013
10 Yemen	Irrigation Improvement Project	P062714	2009
11 Afghanistan	Emergency National Solidarity Project II	P102288	2011
12 India	Andhra Pradesh Rural Poverty Reduction Project	P071272	2012

Source: Authors.

AGRICULTURE GLOBAL PRACTICE TECHNICAL ASSISTANCE PAPER



WORLD BANK GROUP REPORT NUMBER 94753-GLB



1818 H Street, NW
Washington, D.C. 20433 USA
Telephone: 202-473-1000
Internet: www.worldbank.org/agriculture
